

## TO15 RC Outdoor Phase 1 Daily Notes

**Date:** 02/18/2020


**Temperature:** 43.6°F (ambient)

Test starts at 6:46AM, stops at 13:36PM, 620 passes scheduled for today, and total of 2976 passes completed.

Observations:

### West side

TT56 joint west side, no further crack propagation observed compared to 02/14/2020.

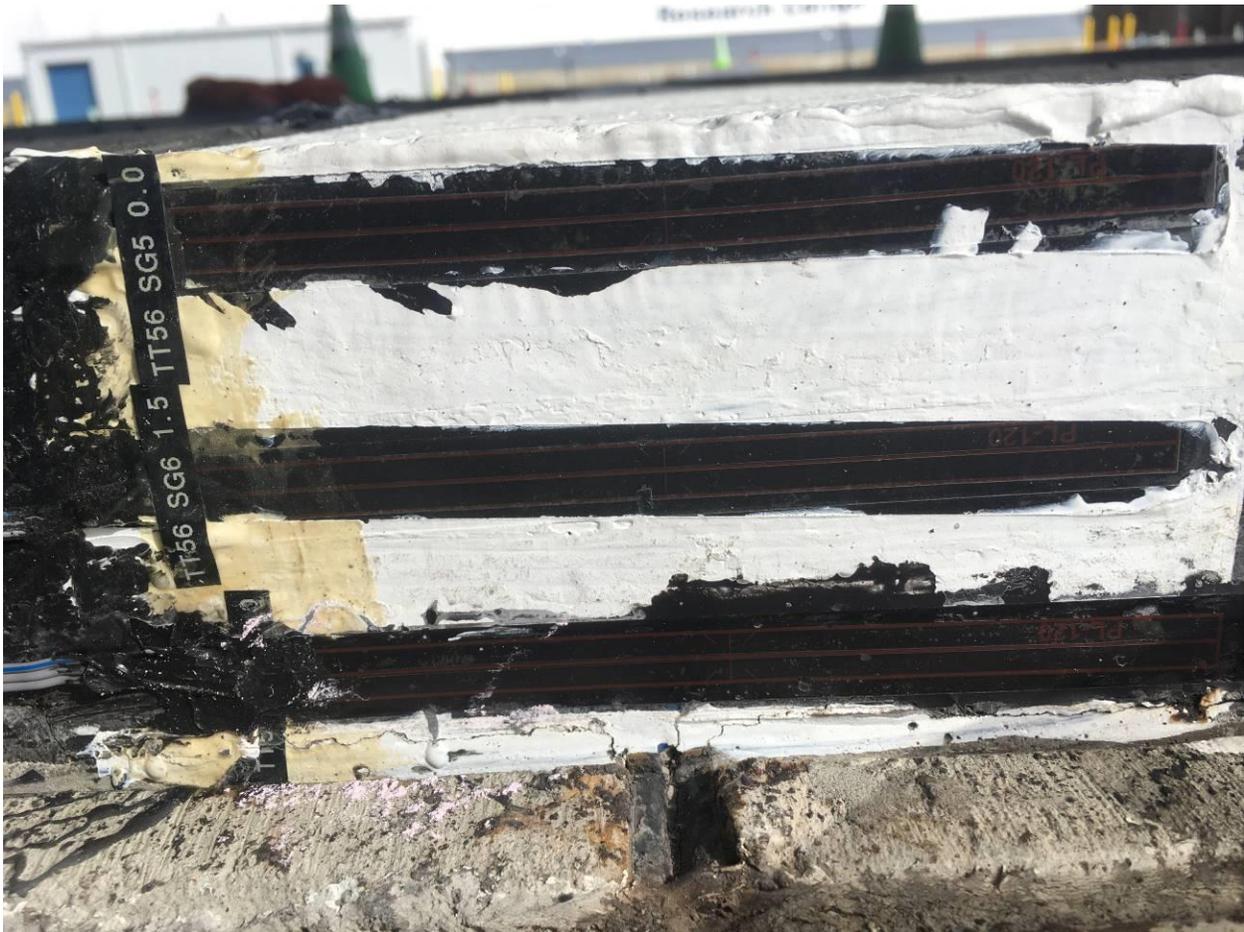

**Figure 1. TT56 Joint**

Bottom up crack at TT45 west vertical edge reaches the height of 1.4 inch, same as 02/14/2020.



Figure 2. TT45 Joint

No crack observed on the TT34 joint.



**Figure 3. TT34 Joint**

No crack observed on TT23 joint.



Figure 4. TT23 Joint

No crack observed on TT12 joint.



Figure 5. TT12 Joint

**East Side**

No crack observed on TT12 joint east side.




**Figure 6. TT12 Joint**

No crack observed on TT23 joint east side.



**Figure 7. TT23 Joint**

No crack observed on TT34 joint east side.

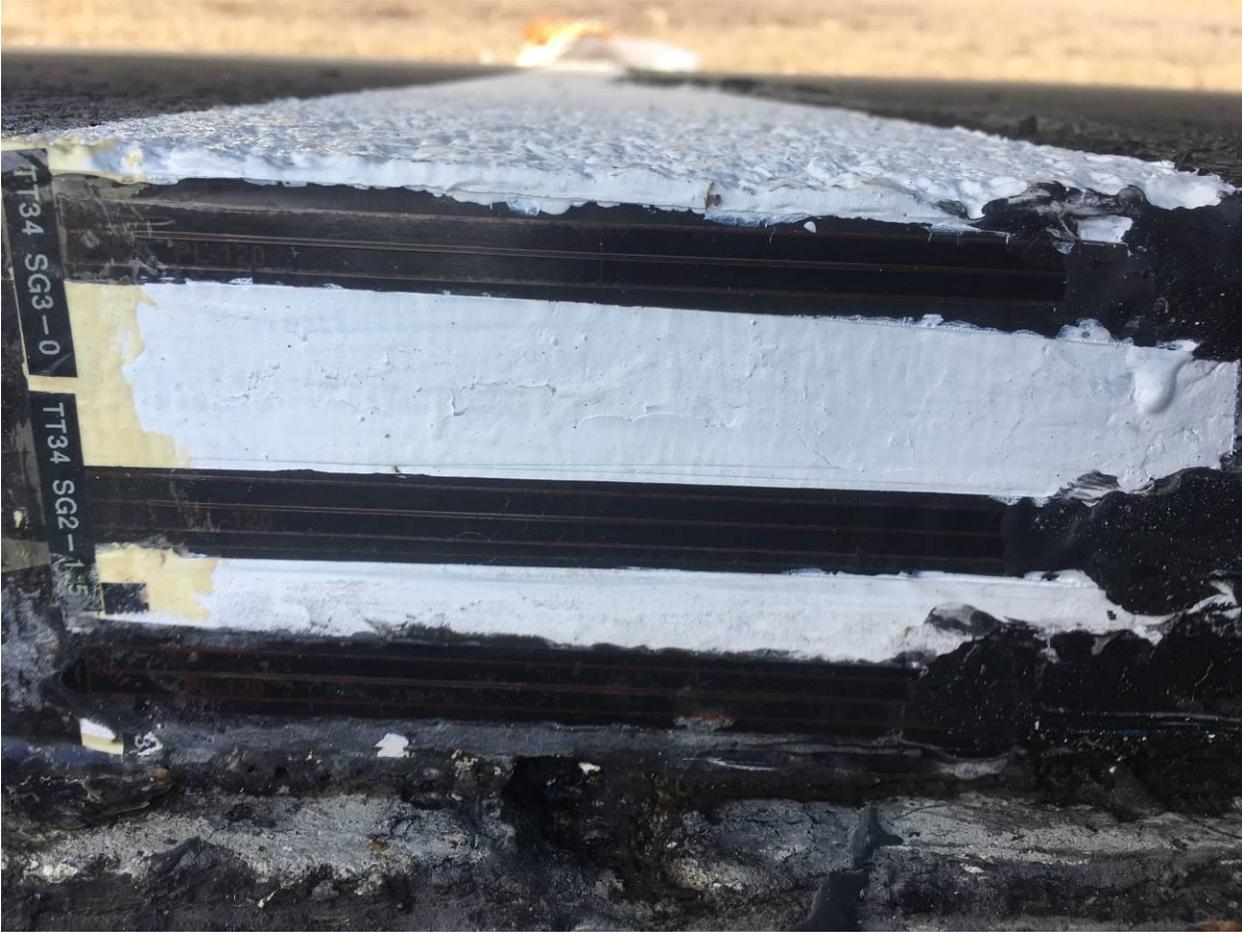


**Figure 8. TT34 Joint**

No crack observed on TT45 joint east side.



**Figure 9. TT45 Joint**

Bottom up crack approximate 4mm height, in asphalt at concrete joint, propagate to the right approximate 30mm parallel to the concrete surface, it shows surface de-bonding but may be just in paint.

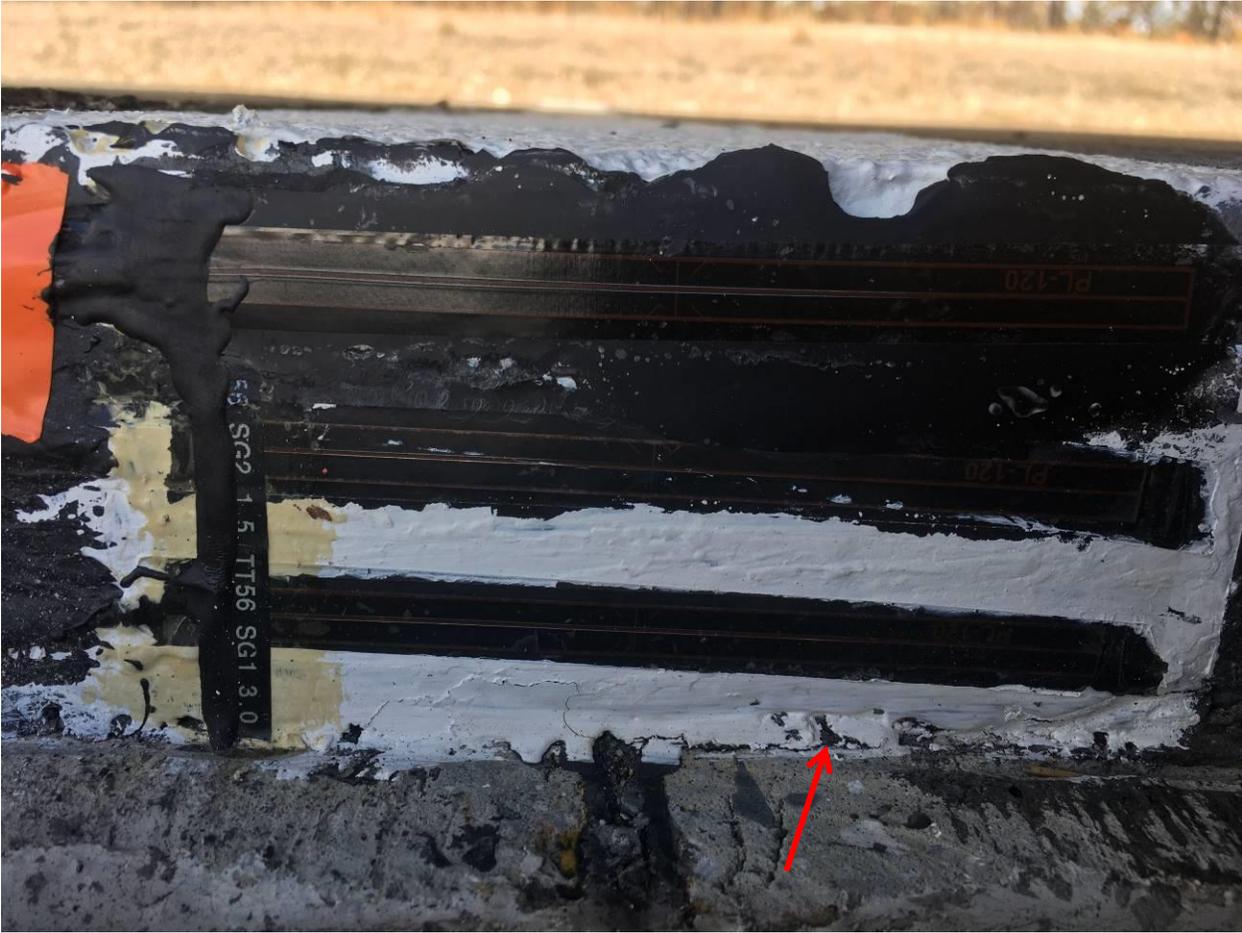

**Figure 10. TT56 Joint**
