

Reflective Cracking Construction Notes

Date: December 11, 2014

Project: Reflective Cracking Indoor Phase IV

Weather:

	6:54 AM	4:47 PM
Temperature (°F):	35.1	32.0
Dew Point (°F):	27.0	28.0
Humidity (%):	72	85
Visibility (Miles):	10.0	10.0
Wind (MPH):	4.6 W	13.8 WSW
Conditions:	Overcast	Overcast

Working Hours: 7:00 AM – 4:30 PM

Sub-Contractor(s): ARA, United Concrete

Personnel: (1) technician (ARA), (1) supervisor, (1) form carpenter (United)

Equipment: Hand tools

Reflective Cracking Construction Notes:

United Concrete continued the installation of the formwork for the Phase IV paving, as shown below in Figure 1.

SRA and ARA personnel installed a new gasket within the center joint of the test rig and moved the two halves of the test rig together to secure it.

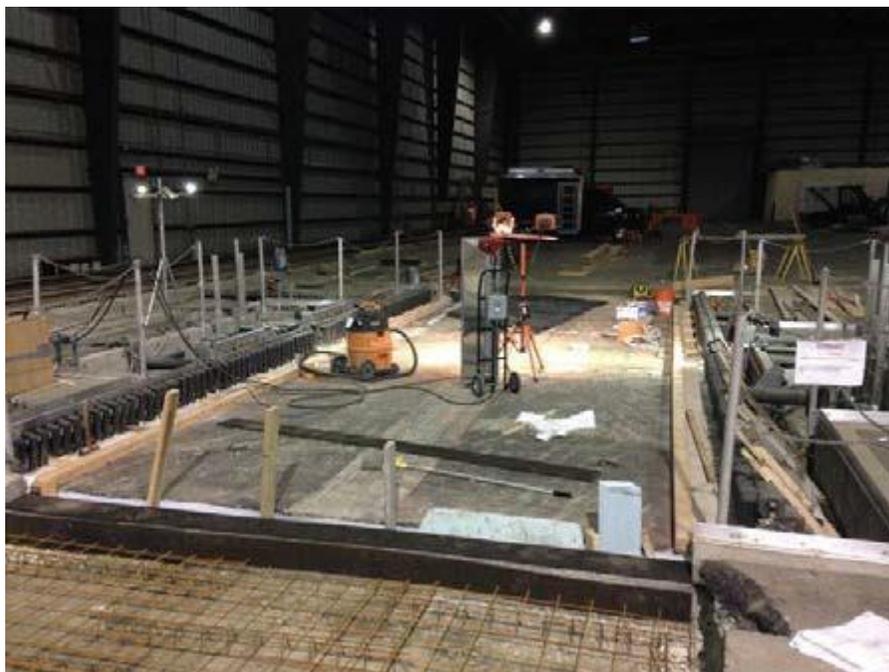


Figure 1. Installation of Formwork Continued.
